

Progress Report

(First Quarter 2014)

Rubik 1709 Project

A Progress Newsletter from Trusthold Development Group SAL (TDG)

Rubik 1709 Progress Report is a newsletter distributed to all Project's Tenants. It is brief news that jointly describes all project's aspects including Project Management, Construction Management, Marketing & Sales and Financial Management.

This issue contains:

- General Overview;
- Construction Brief;
- Site Photos;
- Milestone Schedule;
- Sales summary;
- Upcoming Targets;
- News;



General Overview



Rubik 1709, so far ,has concluded the following achievements:

- 38% of the Project has been sold.
- Shoring and Excavation works have been completed.
- The Constuction Permit has been secured.
- Tender Files/Package I has been launched .
- Milestone Schedule has been finalized.
- Concrete of Blinding under raft foundation has been finalized.



Construction Brief

Shoring and Excavation Works

Shoring and Excavation Works have been completed on November 2013.

Legalization and Permits

As stated earlier, The Construction Permit has been attained as shown below:

	دائرة المبان عدد: ۲۰۱۲/۸۹ ر.م.	- 11. 111 - 1. 1. 1.
	مصلحة الفندسة عدد: ٢٠١٣/٨٢٣	الجمهوم يتماللبنانيته
(7, 12, 2, 1)	عقار: ۱۷۰۹ / الاشرفية د. الله	فسيخلقة طبي الاعطون
200	ارتجصة بنياء	and and an
لمزعموم التطبيقي رقم ١٥٨٧٤ مرد در	وم الإنشار اعنى رقم ۱۱۸ تاريخ ۲۰ /۲۷ /۷۷ ۱۱ /۸ /۸۸ والقانون رقم ۲۶۱ تاريخ ۲۰ /۲۱ /۲۱ /۲۰ وا ۱٫۷۱ تاريخ ۲۰۰۷/۰۸/۱۷ والقانون رقم ۲۰۰۲/۱۷	بناء على القانون رقم ٢٠ /٨٨ كاريخ
1.7.9.		
E		بناءً على الطلب المقدم من شركة الأشر
		بدَّاءً على التعيد الخطي من قبَّل المهندم
Charles and the second s	، الفني عدد ٢٠١٢/٨٩ ر.م. تاريخ ٢٠-٠١ ا بموجب الاصبال رقم ١٠٦٩٦٤٨	
تاريخ ٢٠١٢-١١-٢		وبعد أن استوفيت الرسوم المتوجبة عنه مع ديم
	العانية ومنتة واريعون ملبون ومنتان واويعون الف ليرة تيناتو	
_ تاريخ ٢٠١٢-٢١	ة العلمة للإسكان بموجب ليصال رقم ١٣٣٤٩١	것이상 국가에서 이 문화
	للة على مليون وعشرة الاف ليرة ليناتية	
تاريخ ۲۰۱۴-۱۱-۲۰		وتم تسديد حصمة نقابة المهندسين بموجد
	نان وثلاثون مليون وخمسماية واريعة وعشرون الف ليرة ثبنا	
تاريخ مراجر المري	- NE-11122 M C Y - NE-11122 M	
	job a hel os	in the to be interested
and the second s		حضر موقد من قبل صناعب العلاقة وأبزز
- All .		
The set of	· · · · · · · · · · · · · · · · · · ·	<u>ب</u>
19 B		34 .
展		N.
	-	- 14 16
	1	
at the		
المهندس	h	$\mathcal{A}^{(p)}\mathcal{A}^{(p)}$
مريندائر مزيمتان الهيانو تؤلفجاري	ا رئ	
Chatterfant 1		
المندس باس بشاشة	ية ١٧٠٩ شريعان المدارية الم	a de la coloria
المندس باسر بشائية في هذه الرحصنة وققًا للشروط المفروضية.	ية ١٢٠٠ س-من من الإنشاءات المبينة	
Cite	(all all and	أعطيت هذه الرخصة مع حفظ حقوق ال إعتباراً من هذا التاريخ
	H the last	
ماهند معالی می التولید معالی معالی معا		
		2

Tender Files

Tender file for Package I that is composed of Concrete, waterproofing and MEP associated works have been finalized by our Design Consultants. As such, in November 2013, TDG has launched Tender for Package I.

Nine Qualified Contractors have been chosen where they have submitted their initial offers for executing the above packages. First and second round of negotiation is being performed in order to sign a contract with one of the qualified Contractors.

Design Process

The Architectural and Structural Design are completed . Design of MEP works will be finalized within one month.

Our technical controller, M/s Socotec gave their approval regarding the solidity of the building and the five Safety regulations that have been adopted by our Design Consultants.



Progress of Works on Site

Shoring and Excavation Works have been completed.















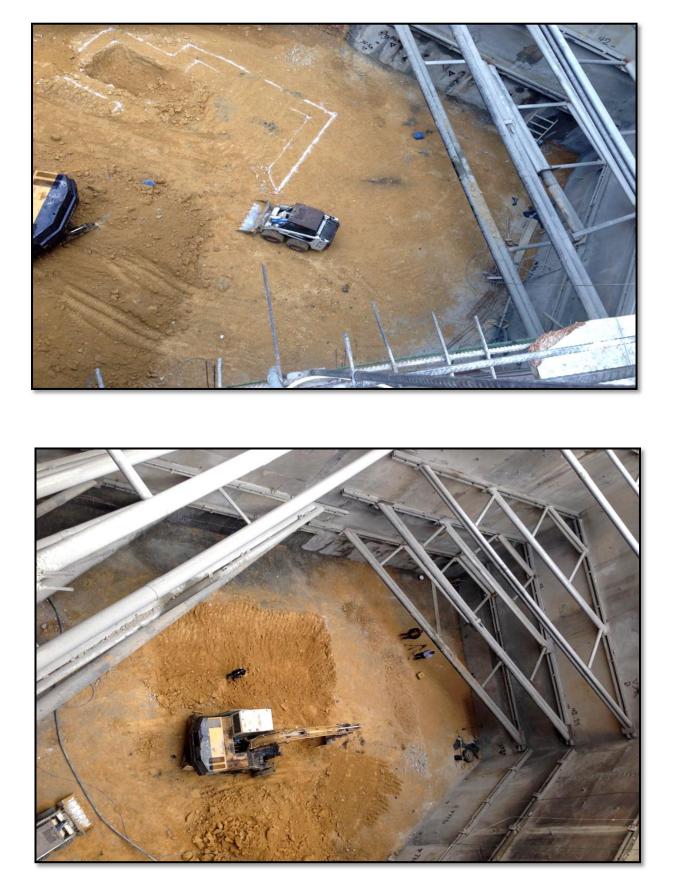



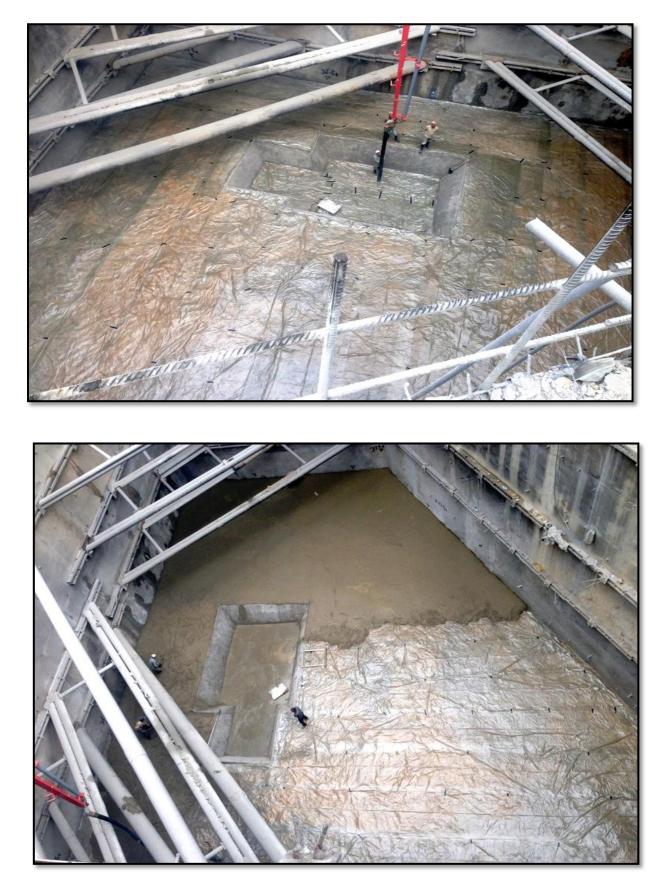







Milestone Schedule

The construction of "RUBIK 1709 Project" will be performed in several stages and will include the following main Milestone Activities as shown in the below table:

Activity Description	Start	Finish
Start of the project	2-Apr-12	
Acquisition of Shoring Permit	2-Apr-12	31-Jan-13
Architectural and Structural Drawings	2-Jul-12	30-Apr-13
Start of Shoring & Excavation works	1-Feb-13	
Shoring & Excavation works	1-Feb-13	30-Nov-13
Tender File(Package I)	1-May-13	1-Nov-13
Budget	1-May-13	29-Jun-13
Master Schedule	1-May-13	1-Apr-14
Tender Launch /Evaluation/Tender Award	1-Oct-13	13-Feb-14
Start Mobilization and Construction works	14-Feb-14	
Reaching Ground Floor	14-Feb-14	15-Oct-14
Reaching 5th Floor	16-Oct-14	16-Jan-15
End Of Structural Concrete works	17-Jan-15	1-Jun-15
Completion of Common Area and Elevation Works	2-Jun-15	1-Jan-16
Completion of Interior works(by tenants)	2-Jan-16	2-Apr-16
Registration of Units	During 2016	
Construction Permit	December 2013	

Completed Activities

On-Progress Activities



Sales Summary

Floor	Unit	Area (m²)		
Basement 1	Showroom 1	290	SOLD	
Gound Floor &	Showroom 2	103/60	AVAILABLE	
Mezzanine	Shop 1	269/177	AVAILABLE	
	Office A	102	SOLD	
1st	Office B	99		
150	Office C	89		
	Office D	96		
Total		306		
	Office A	102		
2-1	Office B	95	SOLD	
2nd	Office C	91	SOLD	
	Office D	96		
Total		384		
	Office A	102		
3rd	Office B	99	COLD.	
	Office C	89	SOLD	
	Office D	96		
Total		386		
	Office A	102	SOLD	
4th	Office B	99		
	Office C	89	SOLD	
	Office D	96		
Total		386		
5th	Office A	102		
	Office B	99	AVAILABLE	
	Office C	89		
	Office D	96		
Total		386		



6th	Office A	102	AVAILABLE	
	Office B	95	AVAILADLE	
	Office C	91	SOLD	
	Office D	96	AVAILABLE	
Total		384		
	Office A	102	AVAILABLE	
7th	Office B	99		
711	Office C	89		
	Office D	96		
Total		386		
	Office A	102		
0.1	Office B	95	AVAILABLE	
8th	Office C	91		
	Office D	96		
Total	-	384	-	
9th	Office A	102		
	Office B	99	AVAILABLE	
	Office C	89		
	Office D	96		
Total	-	386		
1041	Office B	163		
10th	Office C	164	AVAILABLE	
Total		327		
11th	Office B	119	AVAILABLE	
	Office C	107		
Total		226		
12th	Office C	165	AVAILABLE	
Total		165		



Upcoming Targets

Trusthold aims to accomplish the following targets:

- Awarding Package I to a Qualified Contractors.
- Secure the Proceed Permit.
- Commencement of Concrete Works.
- Launching Tender for MEP and Finishing Works.
- Finalization of the Master Schedule.





News

- Facebook for TDG is under preparing. It will be launched in the second quarter of 2014.
- An advertisement for Spears 1858 and Rubik 1709 have been published at "Al-Iktissad Wal-Aamal" Magazine in January 2014 as shown on the right side.
- Construction works at "SPEARS 1858" was commenced on September 2013.

